LEACO RURAL TELEPHONE COOPERATIVE, INC.
REQUEST FOR LIMITED WAIVER AND EXTENSION OF
MOBILITY FUND PHASE I PUBLIC INTEREST OBLIGATIONS

EXHIBIT 1 (UPDATED)

Status of Individual Cell Sites and Waiver Tracts
and
Map of Cell Sites and Waiver Tracts

Status of Individual Cell Sites

Site Name	Census Tract Where Located	Study Area Code Where Located	County	Status Of Site Construction	Census Tracts Impacted By Site Delays
High Lonesome	T35005001200	498002	Chaves	Existing tower. Cell site construction complete. Waiting on electric power turn up. Still require: backhaul construction and Phase 3 work. UPDATE: **Power connected 5/4/15.** Working on: E911 and backhaul, but depends on microwave build to core. Still require: other Phase 3 work.	T35005001200

Site Name	Census Tract Where Located	Study Area Code Where Located	County	Status Of Site Construction	Census Tracts Impacted By Site Delays
Queen	T35015000700	498006	Eddy	Existing tower. Cell site construction complete. Waiting on electric power turn up. Still require: backhaul construction and Phase 3 work. UPDATE: **Power connected 5/4/15.** Working on: E911 and backhaul, but depends on Indian Basin, Illinois Camp, and Lakewood sites. Still require: other Phase 3 work.	T35015000700
Twin Towers	T35005001300	498004	Chaves	Existing tower. Cell site construction complete. Waiting on electric power turn up. Still require: backhaul construction and Phase 3 work. UPDATE: **Power connected 4/21/15. Backhaul constructed.** Working on: E911 and other Phase 3 work.	T35005001300, T35005001400, T35005001102

Site Name	Census Tract Where Located	Study Area Code Where Located	County	Status Of Site Construction	Census Tracts Impacted By Site Delays
Boaz	T35005001200	498002	Chaves	Existing tower. Waiting on Notice to Proceed from tower owner. Still require: cell site construction, electric power, backhaul construction, and Phase 3 work. UPDATE: Still waiting on: NTP, but expected soon now that have permits that depended on county clarification for surveyor. Working on: E911 and backhaul, but cannot test and depends on High Lonesome site. Still require: site construction, power, and Phase 3 work.	T35005001200

Site Name	Census Tract Where Located	Study Area Code Where Located	County	Status Of Site Construction	Census Tracts Impacted By Site Delays
Dunlap	T35005001102	498001	Chaves	Existing tower. Waiting on completion of tower modification and Notice to Proceed from tower owner. Still require: cell site construction, electric power, backhaul construction, and Phase 3 work. UPDATE: **Modification completed 5/6/15.** Waiting on: NTP and determination about migratory bird issues. Working on: E911 and backhaul, but cannot test and depends on microwave build to core. Still require: site construction, power and other Phase 3 work.	T35005001102

Site Name	Census Tract Where Located	Study Area Code Where Located	County	Status Of Site Construction	Census Tracts Impacted By Site Delays
Indian Basin	T35015000700	498006	Eddy	Existing tower. Waiting on Notice to Proceed from tower owner. Still require: cell site construction, electric power, backhaul construction, and Phase 3 work. UPDATE: **Site constructed 4/17/15.** Working on: E911, power, and backhaul, but microwave depends on Illinois Basin and Lakewood sites. Still require: other Phase 3 work.	T35015000700, T35015000900
Lakewood	T35015000900	498008	Eddy	Existing tower. Waiting on completion of tower modification and Notice to Proceed from tower owner. Still require: cell site construction, electric power, backhaul construction, and Phase 3 work. UPDATE: **Received NTP 5/5/15.** Working on: scheduling site construction, backhaul, and power; and E911. Still require: other Phase 3 work.	T35015000900, T35015000700

Site Name	Census Tract Where Located	Study Area Code Where Located	County	Status Of Site Construction	Census Tracts Impacted By Site Delays
White City	T35015000700	498006	Eddy	Existing tower. Waiting on completion of tower modification and Notice to Proceed from tower owner. Still require: cell site construction, electric power, backhaul construction, and Phase 3 work. UPDATE: Still waiting on: tower modification (dispute between landowner and tower owner) and NTP. Working on: E911 and backhaul. Still require: site construction, power, and other Phase 3 work.	T35015000700, T35015000800

Site Name	Census Tract Where Located	Study Area Code Where Located	County	Status Of Site Construction	Census Tracts Impacted By Site Delays
WIPP	T35015000800	498007	Eddy	Existing tower. Waiting on Notice to Proceed from tower owner. Still require: Notice to Proceed from tower owner, cell site construction, electric power, backhaul construction, and Phase 3 work. UPDATE: **Site constructed 4/17/15.** Working on: E911 and backhaul, but microwave depends on Loving transport hub microwave. Still require: power and other Phase 3 work.	T35015000800, T35015000700

Site Name	Census Tract Where Located	Study Area Code Where Located	County	Status Of Site Construction	Census Tracts Impacted By Site Delays
Hagerman Cutoff	T35005001400	498004	Chaves	New tower. Waiting on FCC FONSI. Still require: tower construction, cell site construction, electric power, backhaul construction, and Phase 3 work. UPDATE: **Received FONSI 4/29/15.** Working on: tower construction and backhaul, but cannot test. Still require: site construction, power, and Phase 3 work.	T35005001400, T35005001200, T35015000900

Site Name	Census Tract Where Located	Study Area Code Where Located	County	Status Of Site Construction	Census Tracts Impacted By Site Delays
Hope	T35015000900	498008	Eddy	New tower. Waiting on completion of tower construction. Still require: cell site construction, electric power, backhaul construction, and Phase 3 work. UPDATE: **Tower construction completed 4/29/15.** Waiting on: microwave frequency coordination and power. Working on: site construction, E911, backhaul, but depends on microwave build to core. Still require: other Phase 3 work.	T35015000900, T35005001400

Site Name	Census Tract Where Located	Study Area Code Where Located	County	Status Of Site Construction	Census Tracts Impacted By Site Delays
Illinois Camp	T35015000900	498008	Eddy	New tower. Waiting on BLM approval and lease. Still require: tower construction, Notice to Proceed from tower owner, cell site construction, electric power, backhaul construction, and Phase 3 work. UPDATE: Still waiting on: BLM approval and lease (BLM continues to request different forms or changes on lease, and tower company promptly responds, but BLM not responding to tower communication). Working on: backhaul, but cannot test and microwave depends on Lakewood site. Still require: tower construction, NTP, site construction, power, and Phase 3 work. Exploring: COW (large expense) on private property lease, but need to run propagation.	T35015000900, T35015000700

Site Name	Census Tract Where Located	Study Area Code Where Located	County	Status Of Site Construction	Census Tracts Impacted By Site Delays
Mile Marker 4	T35015000800	498007	Eddy	New tower. Waiting on BLM approval and lease. Still require: tower construction, Notice to Proceed from tower owner, cell site construction, electric power, backhaul construction, and Phase 3 work. UPDATE: Still waiting on: BLM approval and lease (BLM continues to request different forms or changes on lease, and tower company promptly responds, but BLM not responding to tower communication). Working on: backhaul, but cannot test and microwave depends on WIPP and White City sites. Still require: tower construction, NTP, site construction, power, and Phase 3 work.	T35015000800

Site Name	Census Tract Where Located	Study Area Code Where Located	County	Status Of Site Construction	Census Tracts Impacted By Site Delays
Olive	T35005001200	498002	Chaves	New tower. Waiting on success in locating land owner agreeing to lease property and negotiation of lease. Still require: tower construction, Notice to Proceed from tower owner, cell site construction, electric power, backhaul construction, and Phase 3 work. UPDATE: **Still no lease.** Working on: alternate solution with extenders to cover roads that will complete remainder of 75% coverage. Still require: backhaul, power, and Phase 3 work.	T35005001200

Status of Waiver Tracts

Waiver Tract	Study Area Code	County	Sites Required for Completion of Waiver Tract	Eligible Unserved Road Miles in Waiver Tract
35005001102	498001	Chaves	Dunlap, Twin Towers	520.96
35005001200	498002	Chaves	High Lonesome, Boaz, Olive, Hagerman Cutoff	1816.54
35005001400	498004	Chaves	Hagerman Cutoff, Twin Towers, Hope	578.97
35015000700	498006	Eddy	White City, Indian Basin, Queen, WIPP, Illinois Camp, Lakewood	2612.88
35015000800	498007	Eddy	WIPP, Mile Marker 4, White City	980.29
35015000900	498008	Eddy	Illinois Camp, Lakewood, Hope, Indian Basin, Hagerman Cutoff	2801.47
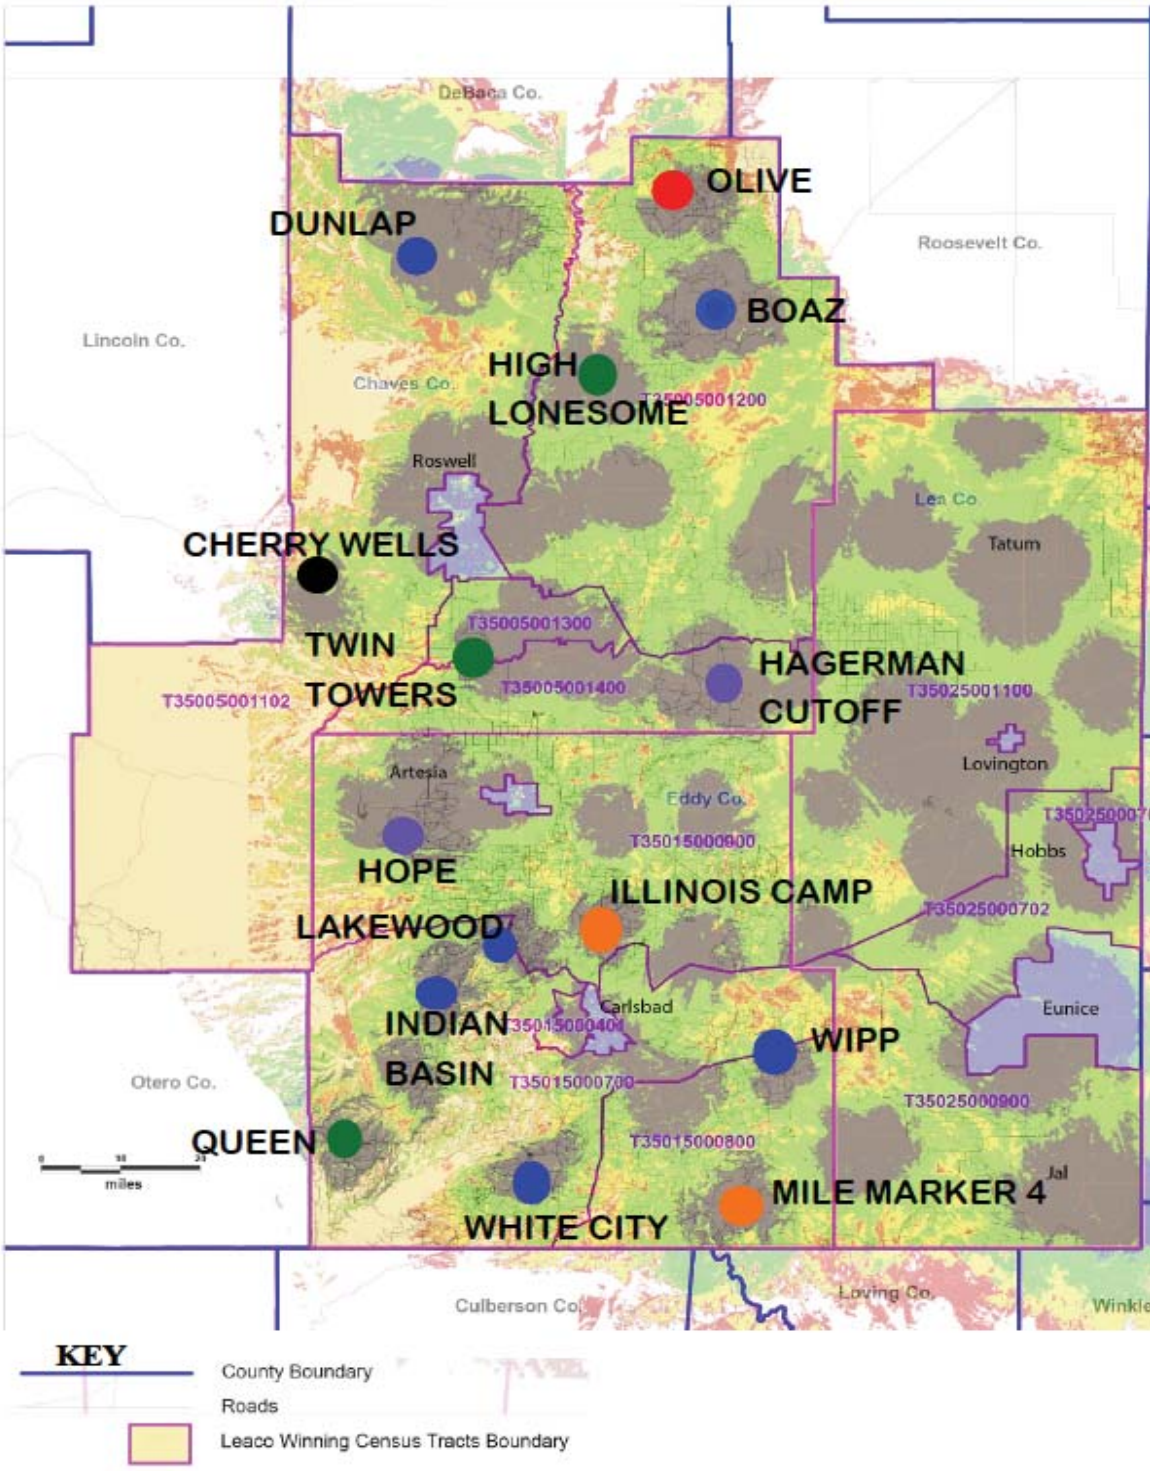
Map of Cell Sites and Waiver Tracts
